

Interconnector Greece-North Macedonia

Project Status Overview

Project Overview

The Project

Total **123km** new HP Pipeline


- 55Km 30" HPP+ 1,5Km 28" HPP, 1 LVS, 3 SS 
- 67km 28" HPP, 5 LVS/SS, Pressure Reduction Station 

New **Border Metering Station** 

- 430.000 Nm3/h
- Bidirectional Design

The Frame

- Intergovernmental Agreement
- Cooperation Agreement Desfa & Nomagas
- Market Test, ARCAs signed
- Joint FID in Oct'2023

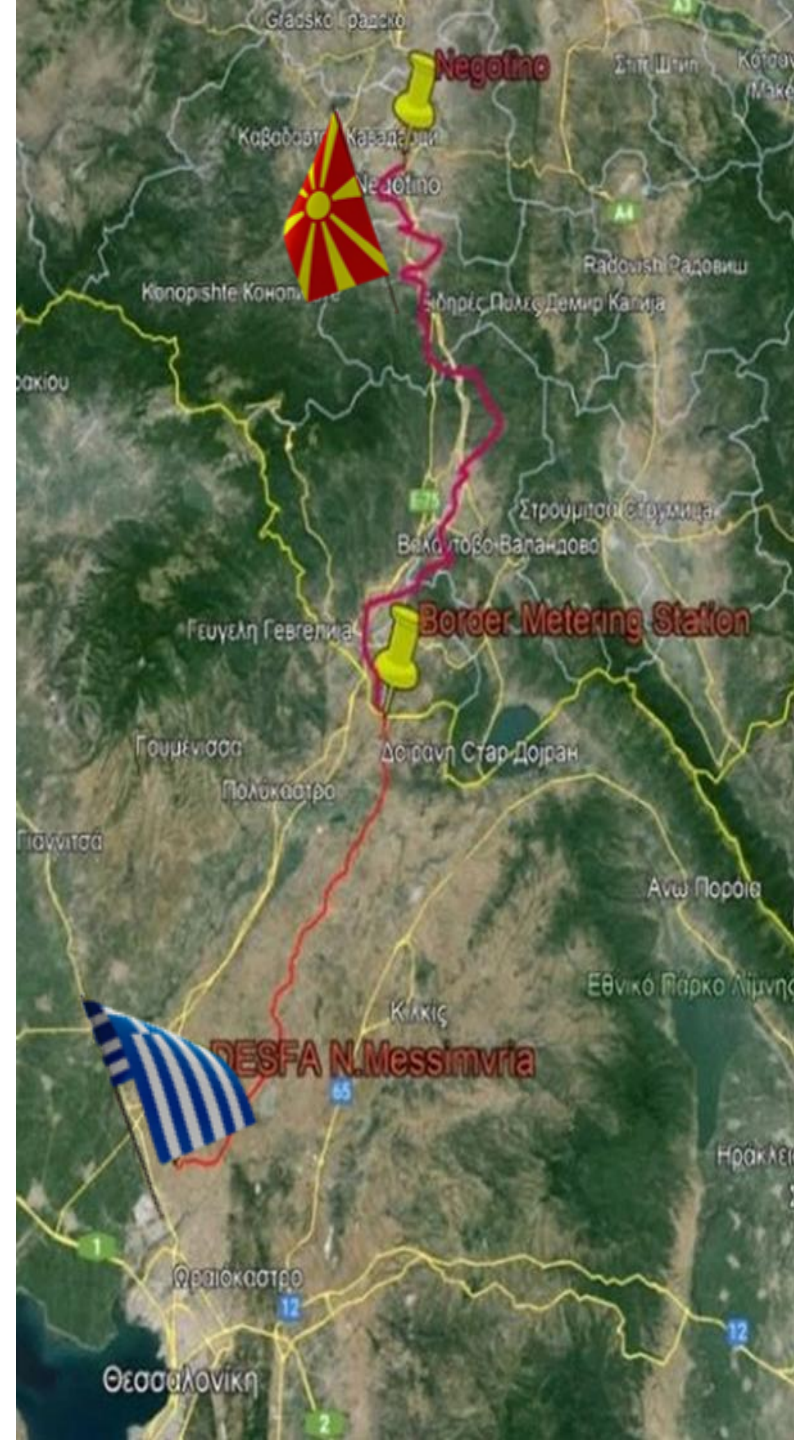

Milestones



- Final Investment Decision
- DESFA-NOMAGAS Agreements
- Tendering
- EPC/Construction Agreements
- Planned completion

FINAL INVESTMENT DECISION FOR THE PROJECT

Oct
2023

Sept
2021

Cooperation
Agreement
DESFA-NER

DESFA
Tender for
Supply of
Pipes

June
2023

DESFA
Tender for
HPP EPC

Aug
2023

Sept
2023

DESFA-
NOMAGAS -
Contract for
Supervision of
Construction in
NM section

Nov
2023

NOMAGAS
Initial Tender for
EPC HPP (incl Pipes)

Sept
2024

DESFA
HPP EPC
award

Oct
2024

NOMAGAS
Tender for EPC HPP
(incl Pipes)

May
2025

NOMAGAS-
EPC AWARD

DESFA
BORDER STATION
AWARD

Q3
2026

PLANNED
COMPLETION
GR PART

Q1
2027

PLANNED
COMPLETION
NM PART

(under
replanning)

• 2021

• 2023

• 2024


• 2025

• 2026

• 2027

Current status – Greek part

Completed works

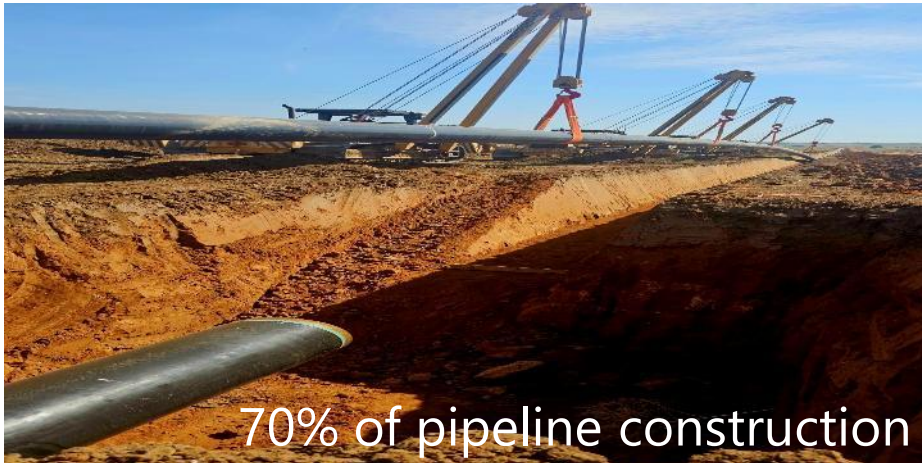

Current status – Greek part



INTERCONNECTOR GREECE – NORTH MACEDONIA



| May 2026

Current status – Greek part



INTERCONNECTOR GREECE – NORTH MACEDONIA



| May 2026

Current status – North Macedonian part


Completed works:

- 7% of pipeline construction
- 100% of pipes production

Pipeline installation works commenced in JAN'2026



Current status – North Macedonian part

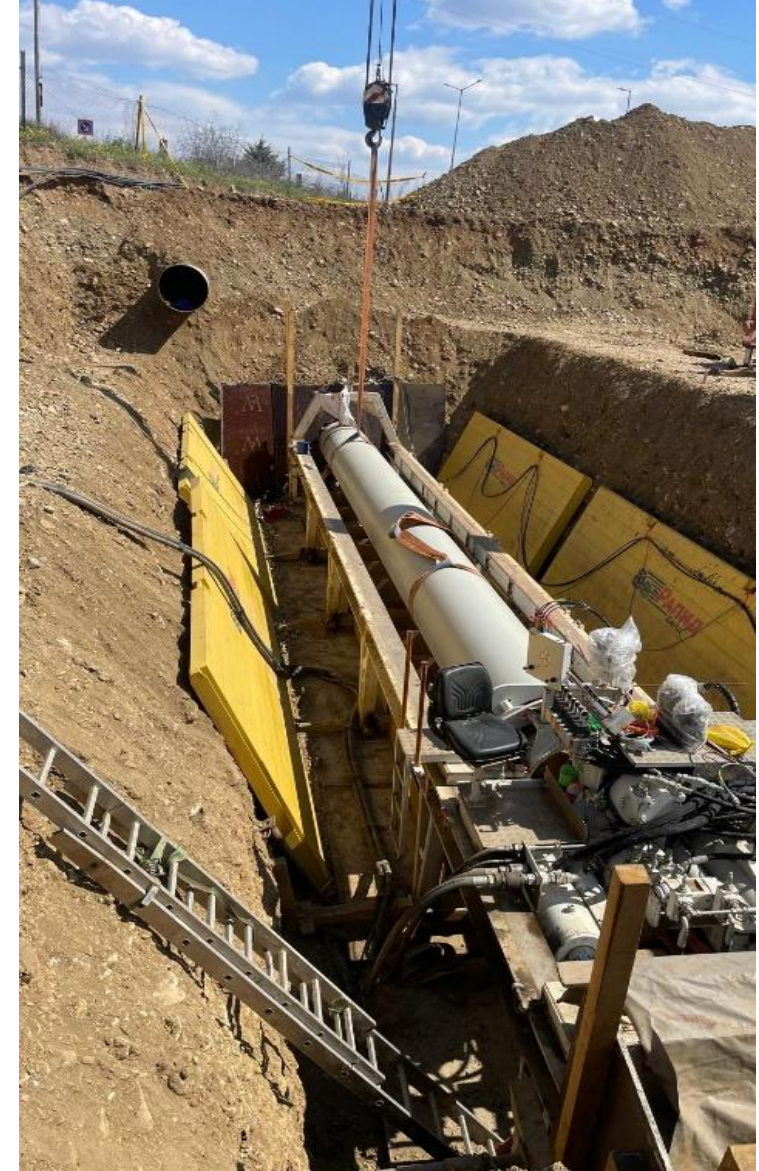

Current status – North Macedonian part



INTERCONNECTOR GREECE – NORTH MACEDONIA



| May 2026

THANK YOU

